R.A. Bill No: 2nd & part:

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measuremer
1	2	Number 3	Length 4	Breadth 5	Depth 6	7	8
	Name of work :- Package "9" : (a) Improvements of Drains @ Thirumenahalli village main Road in ward No: 05- b) Improvements of Roads & Drains at Thirumenahalli junction to Agrahara layout Govt Hospital in ward No: 05- (c) -do- at Cholekanahalli village main Road & Cross Roads in ward No: 05- (d) -do- Markandeya nagara main Roads & Cross Roads in ward No: 05. (e) -do- Siraj layout main Roads & cross Roads in ward No: 05- (f) -do- Kogilu Surrounding in ward No: 05: (g) -do- Agrahara village cross road in ward No: 05-.						

M. A. R. 57 (Rule 116) **No. D**

Measurement Book

17908

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Number	Dimensions Length	Breadth	Depth	Contents	Reference to last Measurement
	2	3	4	5	6	7	8
	Improvements to Roads and drain at Agrahara layout Kallappa reddy main Road in ward No: 05, Byatarayanapura Sub Division.						
	EE NO: 005-18-000038, 005-18-000039, 005-18-000020, 005-18-000022, 005-18-000023, 005-18-000024 005-18-000031 & 005-18-000033.						
	Est cost: 285-00 Lacs.						
	Survey: Sri. S.K. Chandra.						
	AE NO: EE/project/Ag. NO: 200/17-18				Dt:	23/03/2018	
	AEE NO: EE (project)/YNK zone/NO/200/17-18				Dt:	23/03/2018	

M. A. R. 57 (Rule 116) **No. D**

Measurement Book

17912

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Number	Dimensions Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
	Item No: (10): providing and laying hot applied thermoplastic Compound 2.5 mm thick including reflectorizing glass beads 250 gms/sqm area etc complete as per Specification.						
	Qty vide measurement Sheet p.no: (19)					592.94 sqmt	
		@ Rs. 602.42/sqmt				⟹	3,57,199.41
						Total Rs.	67,84,450.48
							67,84,666.00
	Certified that the above work has been Carriedout Satisfactorily as per Specification.					Asundress	
							29/05/2018.

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8

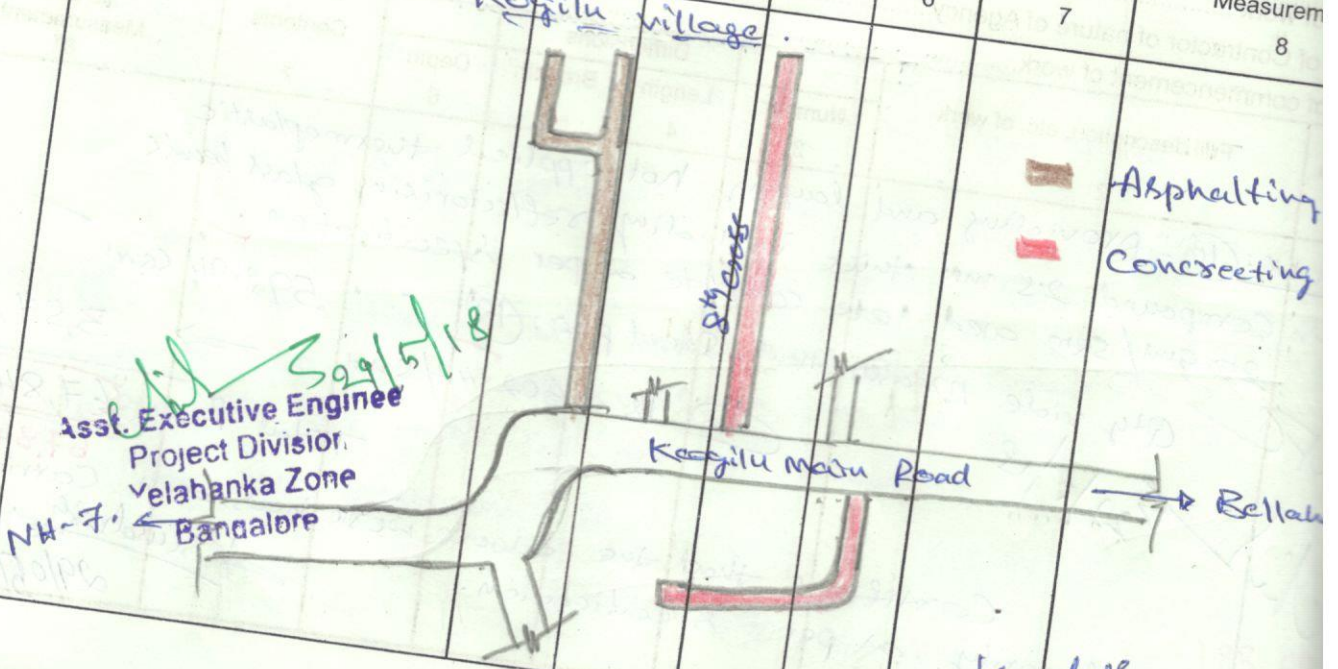

29/5/18
Asst. Executive Engineer
Project Division
Yelahanka Zone

29/5/18

M. A. R. 57 (Rule 116) **No. D**

Measurement Book

17913

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Number	Dimensions: Length	Dimensions: Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8

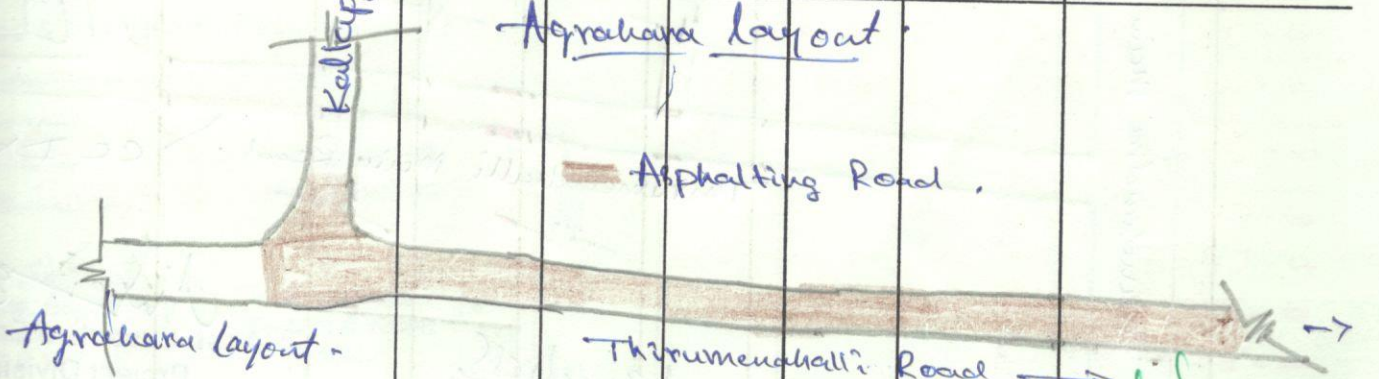

Agrahara layout.

Asphalting Road.

Kalliappa Reddy Road

Thirumenahalli Road →

Agrahara layout.

LAKE.

Asst. Executive Engineer
Project Division.
Yelahanka Zone
Bangalore

29/5/18

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Thanisandra Main Road						
	Thirumenahalli village.						
	Govt s						
	Thirumenahalli Main Road.						
	CC Drain.						
	Measurement						
29/5/18.							
	Asst. Executive Engineer Project Division Yelahanka Zone Bangalore						

M. A. R. 57 (Rule 116) **No. D** 17914

Measurement Book

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Number	Dimensions: Length	Dimensions: Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
	Audited & Admitted for Rs. Rs: 67,84,666-00 Rs: 64,75,752-00 by Cheque and Rs. 3,08,914:- by Adjustment					Total B.N Rs: 2,06,16,180-00 Less part Bill Rs: 138,31,514-00 Less part Bill Rs: 67,84,666-00 1% IT- 67847-00 1% Cess- 67847-00 0.1% CBF 6785-00 LR. 166435-00 Adju - 3,08,914-00 Cheque: 64,75,752-00	

Accts. Supdt. Project Division B.B.M.P. 06/07

Exe. Engineer Project Division B.B.M.P 7/7/18
